



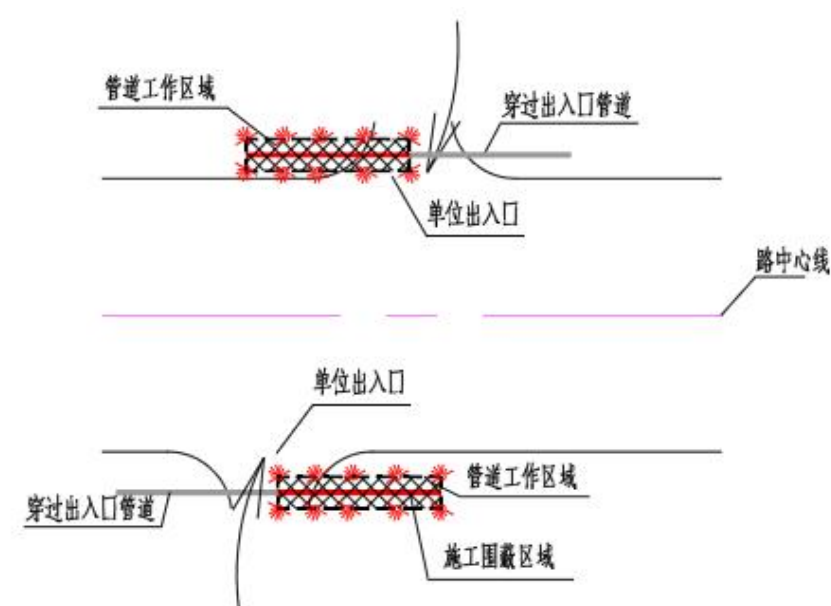

图：路口与单位出入口施工围蔽阶段二示意图

④路口与单位出入口施工：横过路口或单位出入口的管线施工一般采用倒边施工，在保证路段通行能力的情况下分两段或多段进行围蔽施工，车流则从围蔽区域另外一侧绕行。

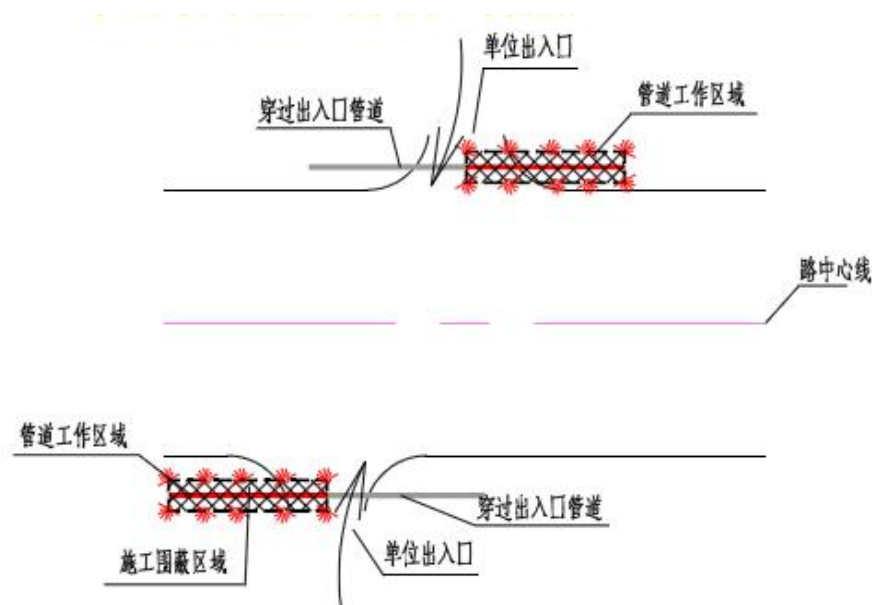

Technical drawing of a metal frame structure. The overall dimensions are 1500mm in width and 1000mm in height. The internal width is 800mm and the internal height is 200mm. The legs are spread out at the bottom, with a spread of 420mm. The frame is made of black metal tubing with yellow reflective tape on the top and bottom rails.

C2:常规铁马围蔽示意图

批准 Ratified			设计 Designed	李昊	金广源	项目负责人 Project Principal	冯雄力	冯雄力	 华设设计集团股份有限公司 China Design Group Co.,Ltd	分项名称 Sub-Project Title	交通工程	项目编号 Project NO.	20220501			
审定 Approved			绘图 Drawing	李昊	金广源	专业负责人 Principal Designer	时磊	时磊		分项编号 Sub-Project NO.	01	版本号 Edition No.	A			
审核 Reviewed	时磊	时磊	交通工程设计说明							建设单位 Client	韶关市曲江水务投资有限公司	比 例 Scale		设计阶段 Project Phase	施工图设计	
复核 Reviewed	黄达	黄达								项目名称 Project Name	曲江城区供水旧管网改造与新城区扩管工程——穿城北江右标段	日 期 Date	2024.03	图 号 Drawing No.	JT-SM	
